

ID	Task Name	Duration	Start	Finish	08
					e a p a u Jul u e c o e
1	osd11-dev-schedule	171 days?	Mon 08-3-17	Mon 08-11-10	
2	OSD 1.0/1.1 Production Releases	75 days	Fri 08-5-2	Thu 08-8-14	
3	AZ 3.0	40 days	Fri 08-5-2	Thu 08-6-26	
4	Feature freeze	0 days	Fri 08-5-2	Fri 08-5-2	
5	Alpha1 release	0 days	Fri 08-5-23	Fri 08-5-23	
6	Bug fix and testing (alpha1)	5 days	Fri 08-5-23	Thu 08-5-29	
7	Alpha2 release	0 days	Thu 08-5-29	Thu 08-5-29	
8	Bug fix and testing (alpha2)	5 days	Fri 08-5-30	Thu 08-6-5	
9	Beta release	0 days	Thu 08-6-5	Thu 08-6-5	
10	Bug fix and testing(beta)	5 days	Fri 08-6-6	Thu 08-6-12	
11	Production release(EN)	0 days	Thu 08-6-12	Thu 08-6-12	
12	Production release(Multi Lang)	10 days	Fri 08-6-13	Thu 08-6-26	
13	AZ 4.0	30 days	Fri 08-6-6	Thu 08-7-17	
14	Feature freeze	0 days	Fri 08-6-6	Fri 08-6-6	
15	Alpha1 release	0 days	Fri 08-6-27	Fri 08-6-27	
16	Bug fix and testing (alpha1)	5 days	Fri 08-6-27	Thu 08-7-3	
17	Alpha2 release	0 days	Thu 08-7-3	Thu 08-7-3	
18	Bug fix and testing (alpha2)	5 days	Fri 08-7-4	Thu 08-7-10	
19	Beta release	0 days	Thu 08-7-10	Thu 08-7-10	
20	Bug fix and testing(beta)	5 days	Fri 08-7-11	Thu 08-7-17	
21	Production release	0 days	Thu 08-7-17	Thu 08-7-17	
22	AZ 5.0	30 days	Fri 08-7-4	Thu 08-8-14	
31	OSD 1.0/1.1 Development And Feature Releases	171 days?	Mon 08-3-17	Mon 08-11-10	
32	P1	69 days?	Mon 08-3-17	Thu 08-6-19	
33	Choose first boot language support Latin	69 days?	Mon 08-3-17	Thu 08-6-19	
34	Technical design	1 day	Mon 08-3-17	Mon 08-3-17	
35	Implementation	14 days	Tue 08-5-6	Fri 08-5-23	
36	Finish language pack(French)	5 days	Thu 08-6-12	Wed 08-6-18	
37	Finish language pack(other Latin)	1 day?	Thu 08-6-19	Thu 08-6-19	
38	Choose first boot language support Asia	50 days?	Mon 08-3-17	Fri 08-5-23	

Project: osd11-dev-schedule
Date: Tue 08-6-3

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline

Nerochiaro
Xiamen Team

ID	Task Name	Duration	Start	Finish	08
					e a p a u Jul u e c o e
39	Technical design	1 day	Mon 08-4-21	Mon 08-4-21	
40	Implementation	24 days	Tue 08-4-22	Fri 08-5-23	
41	Finish language pack(Asia)	1 day?	Mon 08-3-17	Mon 08-3-17	
42	Copy settings/sched rec/YouTube on upgrade from TORFU to AZ	22 days	Thu 08-4-24	Fri 08-5-23	
43	GUI design	17 days	Thu 08-4-24	Fri 08-5-16	
44	Technical design	17 days	Thu 08-4-24	Fri 08-5-16	
45	Implementation	5 days	Mon 08-5-19	Fri 08-5-23	
46	P2	76 days	Mon 08-4-14	Mon 08-7-28	
47	Video Database/Cover Art	68 days	Mon 08-4-14	Wed 08-7-16	
48	Functional and GUI design	8 days	Mon 08-4-14	Wed 08-4-23	
49	Technical design	35 days	Thu 08-5-15	Wed 08-7-2	
50	step1~3	25 days	Thu 08-5-15	Wed 08-6-18	
51	step4	10 days	Thu 08-6-19	Wed 08-7-2	
52	Implementation	45 days	Thu 08-5-15	Wed 08-7-16	
53	step1~3	30 days	Thu 08-5-15	Wed 08-6-25	
54	step3	15 days	Thu 08-6-26	Wed 08-7-16	
55	Thumbnails for (recorded) video(screen shot)	2 days	Thu 08-7-17	Fri 08-7-18	
56	Technical design	1 day	Thu 08-7-17	Thu 08-7-17	
57	Implementation	1 day	Fri 08-7-18	Fri 08-7-18	
58	Play back subtitle	33 days	Mon 08-4-14	Wed 08-5-28	
59	Functional and GUI design	3 days	Mon 08-4-14	Wed 08-4-16	
60	Technical design	5 days	Mon 08-4-14	Fri 08-4-18	
61	Implementation	28 days	Mon 08-4-21	Wed 08-5-28	
62	Thumbnail speed up(bz 2579)	6 days	Mon 08-7-21	Mon 08-7-28	
63	Technical design	1 day	Mon 08-7-21	Mon 08-7-21	
64	Implementation	5 days	Tue 08-7-22	Mon 08-7-28	
65	P3	37 days	Fri 08-6-27	Mon 08-8-18	
82	Unprioritized	60 days	Mon 08-8-18	Mon 08-11-10	

Project: osd11-dev-schedule
Date: Tue 08-6-3

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Resource Names	il 21	July 1			September
						5-5	6-9	7-14	8-18	9-22
1	SW Development	140 days?	Mon 08-5-26	Fri 08-12-5						
2	Startup: board release support	5 days	Mon 08-5-26	Mon 08-6-2						
5	Phase I: bsp and basic multimedia	35 days?	Mon 08-6-2	Fri 08-7-18						
6	Production support	10 days	Mon 08-6-2	Fri 08-6-13	Frank,Terry					
7	Mac/SN mgmt tools	10 days	Mon 08-6-2	Fri 08-6-13						
8	Disk management	14 days	Mon 08-6-2	Thu 08-6-19	John,Terry					
9	SD/MMC card and USB hotplug	5 days	Mon 08-6-2	Fri 08-6-6						
10	Disk format	5 days	Mon 08-6-9	Fri 08-6-13						
11	VFAT/ext3 support	2 days	Mon 08-6-16	Tue 08-6-17						
12	Multipartition support	2 days	Wed 08-6-18	Thu 08-6-19						
13	USB sub-system	25 days	Mon 08-6-2	Fri 08-7-4	Frank					
14	USB host DMA support	5 days	Mon 08-6-2	Fri 08-6-6						
15	Wifi support	20 days	Mon 08-6-9	Fri 08-7-4						
16	IR sub-system & RTC	10 days	Mon 08-7-7	Fri 08-7-18	John					
17	IR Learning/Blaster	10 days	Mon 08-7-7	Fri 08-7-18						
18	Subsystem test code base release	0 days	Fri 08-7-18	Fri 08-7-18						
19	AV Drivers	31 days?	Mon 08-6-2	Mon 08-7-14						
20	HDMI output	25 days	Tue 08-6-10	Mon 08-7-14	Jimmy					
21	u-boot support	10 days	Tue 08-6-10	Mon 08-6-23						
22	kernel support	15 days	Tue 08-6-24	Mon 08-7-14						
23	V4L2	12 days?	Mon 08-6-2	Tue 08-6-17	Steven,Bob					
24	composite capture	5 days	Mon 08-6-2	Fri 08-6-6						
25	component capture	5 days	Mon 08-6-9	Fri 08-6-13						
26	media encrypt system	1 day?	Mon 08-6-16	Mon 08-6-16						
27	HD input, SVGA capture, SD output?	1 day?	Tue 08-6-17	Tue 08-6-17						
28	TI command line multimedia	5 days	Wed 08-6-18	Tue 08-6-24	Steven					
29	demo playback	3 days	Wed 08-6-18	Fri 08-6-20						
30	demo recording	2 days	Mon 08-6-23	Tue 08-6-24						
31	Phase II: VLC multimedia and Applications	100 days	Mon 08-5-26	Fri 08-10-10						
32	VLC	95 days	Mon 08-6-2	Fri 08-10-10	JeanPaul					

Project: osd20-dev-schedule
Date: Tue 08-6-3

Task

Milestone

External Tasks

Split

Summary

External Milestone

Progress

Project Summary

Deadline

ID	Task Name	Duration	Start	Finish	Resource Names	il 21	July 1			September
						5-5	6-9	7-14	8-18	9-22
33	Dev system setup	10 days	Mon 08-6-2	Fri 08-6-13						
34	Basic playback and recording	39 days	Mon 08-6-16	Thu 08-8-7						
35	playback	15.5 days	Mon 08-6-16	Mon 08-7-7						
36	VLC to ARM9	5 days	Mon 08-6-16	Fri 08-6-20						
37	DSP decoder module	10 days	Mon 08-6-23	Fri 08-7-4						
38	PCM audio decoder	0.5 days	Mon 08-7-7	Mon 08-7-7						
39	recording	18.5 days	Mon 08-7-7	Thu 08-7-31						
40	FB from duplicate chain	4 days	Mon 08-7-7	Fri 08-7-11						
41	V4L2 testing and bugfixing	3 days	Fri 08-7-11	Wed 08-7-16						
42	Extend DBUS interface	1 day	Wed 08-7-16	Thu 08-7-17						
43	DSP encoding module	10 days	Thu 08-7-17	Thu 08-7-31						
44	Audio encoding linear PCM	0.5 days	Thu 08-7-31	Thu 08-7-31						
45	Milestone delivery	5 days	Fri 08-8-1	Thu 08-8-7						
46	Demo integration	5 days	Fri 08-8-1	Thu 08-8-7						
47	Testing	2 days	Fri 08-8-1	Mon 08-8-4						
48	DBUS and full playback support	22.5 days	Fri 08-8-8	Tue 08-9-9						
49	Audio decoder support	17.5 days	Fri 08-8-8	Tue 08-9-2						
50	Tremor audio decoder	1 day	Fri 08-8-8	Fri 08-8-8						
51	WMA audio decoder	5 days	Mon 08-8-11	Fri 08-8-15						
52	AC3 audio decoder	5 days	Mon 08-8-18	Fri 08-8-22						
53	AAC audio decoder	5 days	Mon 08-8-25	Fri 08-8-29						
54	Flac audio decoder	1 day	Mon 08-9-1	Mon 08-9-1						
55	MP3 audio decoder	0.5 days	Tue 08-9-2	Tue 08-9-2						
56	Milestone delivery	5 days	Tue 08-9-2	Tue 08-9-9						
57	Player integration	5 days	Tue 08-9-2	Tue 08-9-9						
58	Testing	3 days	Tue 08-9-2	Fri 08-9-5						
59	Full recording support	19.5 days	Tue 08-9-9	Mon 08-10-6						
60	Audio encoder support	14.5 days	Tue 08-9-9	Mon 08-9-29						
61	Audio encoding MPEG1/2 layer 1,2	4 days	Tue 08-9-9	Mon 08-9-15						
62	Audio encoding MP3	5 days	Mon 08-9-15	Mon 08-9-22						

Project: osd20-dev-schedule
Date: Tue 08-6-3




ID	Task Name	Duration	Start	Finish	Resource Names	il 21	July 1			September
						5-5	6-9	7-14	8-18	9-22
63	Audio encoding MPEG-4 AAC-LC	5 days	Mon 08-9-22	Mon 08-9-29						
64	Audio encoding G726	0.5 days	Mon 08-9-29	Mon 08-9-29						
65	Milestone delivery	5 days	Tue 08-9-30	Mon 08-10-6						
66	Recorder integration	5 days	Tue 08-9-30	Mon 08-10-6						
67	Testing	5 days	Tue 08-9-30	Mon 08-10-6						
68	System integration	4 days	Tue 08-10-7	Fri 08-10-10						
69	Video monitor	1 day	Tue 08-10-7	Tue 08-10-7						
70	Playback (play/pause/trickplay)	1 day	Wed 08-10-8	Wed 08-10-8						
71	Recording	1 day	Thu 08-10-9	Thu 08-10-9						
72	Meta-data (media info)	1 day	Fri 08-10-10	Fri 08-10-10						
73	Qt	30 days	Mon 08-5-26	Fri 08-7-4	Tom					
74	Qt Porting	15 days	Mon 08-5-26	Fri 08-6-13						
75	Menu system porting	10 days	Mon 08-6-16	Fri 08-6-27						
76	DBUS support	5 days	Mon 08-6-30	Fri 08-7-4						
77	Applications	45 days	Mon 08-7-7	Fri 08-9-5	Nick,Wesley,Gorde					
78	3rd party app support framework design	5 days	Mon 08-7-7	Fri 08-7-11						
79	Applications porting	40 days	Mon 08-7-14	Fri 08-9-5						
80	Phase III: System integration	125 days	Mon 08-6-2	Fri 08-11-21						
81	Open Embedded Build system	25 days	Mon 08-6-2	Fri 08-7-4	Tom					
82	Open Embedded	15 days	Mon 08-6-2	Fri 08-6-20						
83	Recipe creation and porting	5 days	Mon 08-6-23	Fri 08-6-27						
84	rootfs creation	5 days	Mon 08-6-30	Fri 08-7-4						
85	Package SW updater	20 days	Mon 08-7-7	Fri 08-8-1	Tom					
86	ipkg support	20 days	Mon 08-7-7	Fri 08-8-1						
87	Integration and release	30 days	Mon 08-10-13	Fri 08-11-21						
88	System integration	20 days	Mon 08-10-13	Fri 08-11-7						
89	Alpha release	0 days	Fri 08-11-7	Fri 08-11-7						
90	Beta release	10 days	Mon 08-11-10	Fri 08-11-21						
91	Production release	0 days	Fri 08-11-21	Fri 08-11-21						
92	Phase IV: Advanced features	10 days	Mon 08-11-24	Fri 08-12-5						

Project: osd20-dev-schedule
Date: Tue 08-6-3



11	November 21		February 1		April 11		June 21		September 1		November 11		January 21		April 1		June 11		August 21	
10-27	12-1	1-5	2-9	3-16	4-20	5-25	6-29	8-3	9-7	10-12	11-16	12-21	1-25	3-1	4-5	5-10	6-14	7-19	8-23	9-27

Project: osd20-dev-schedule Date: Tue 08-6-3	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

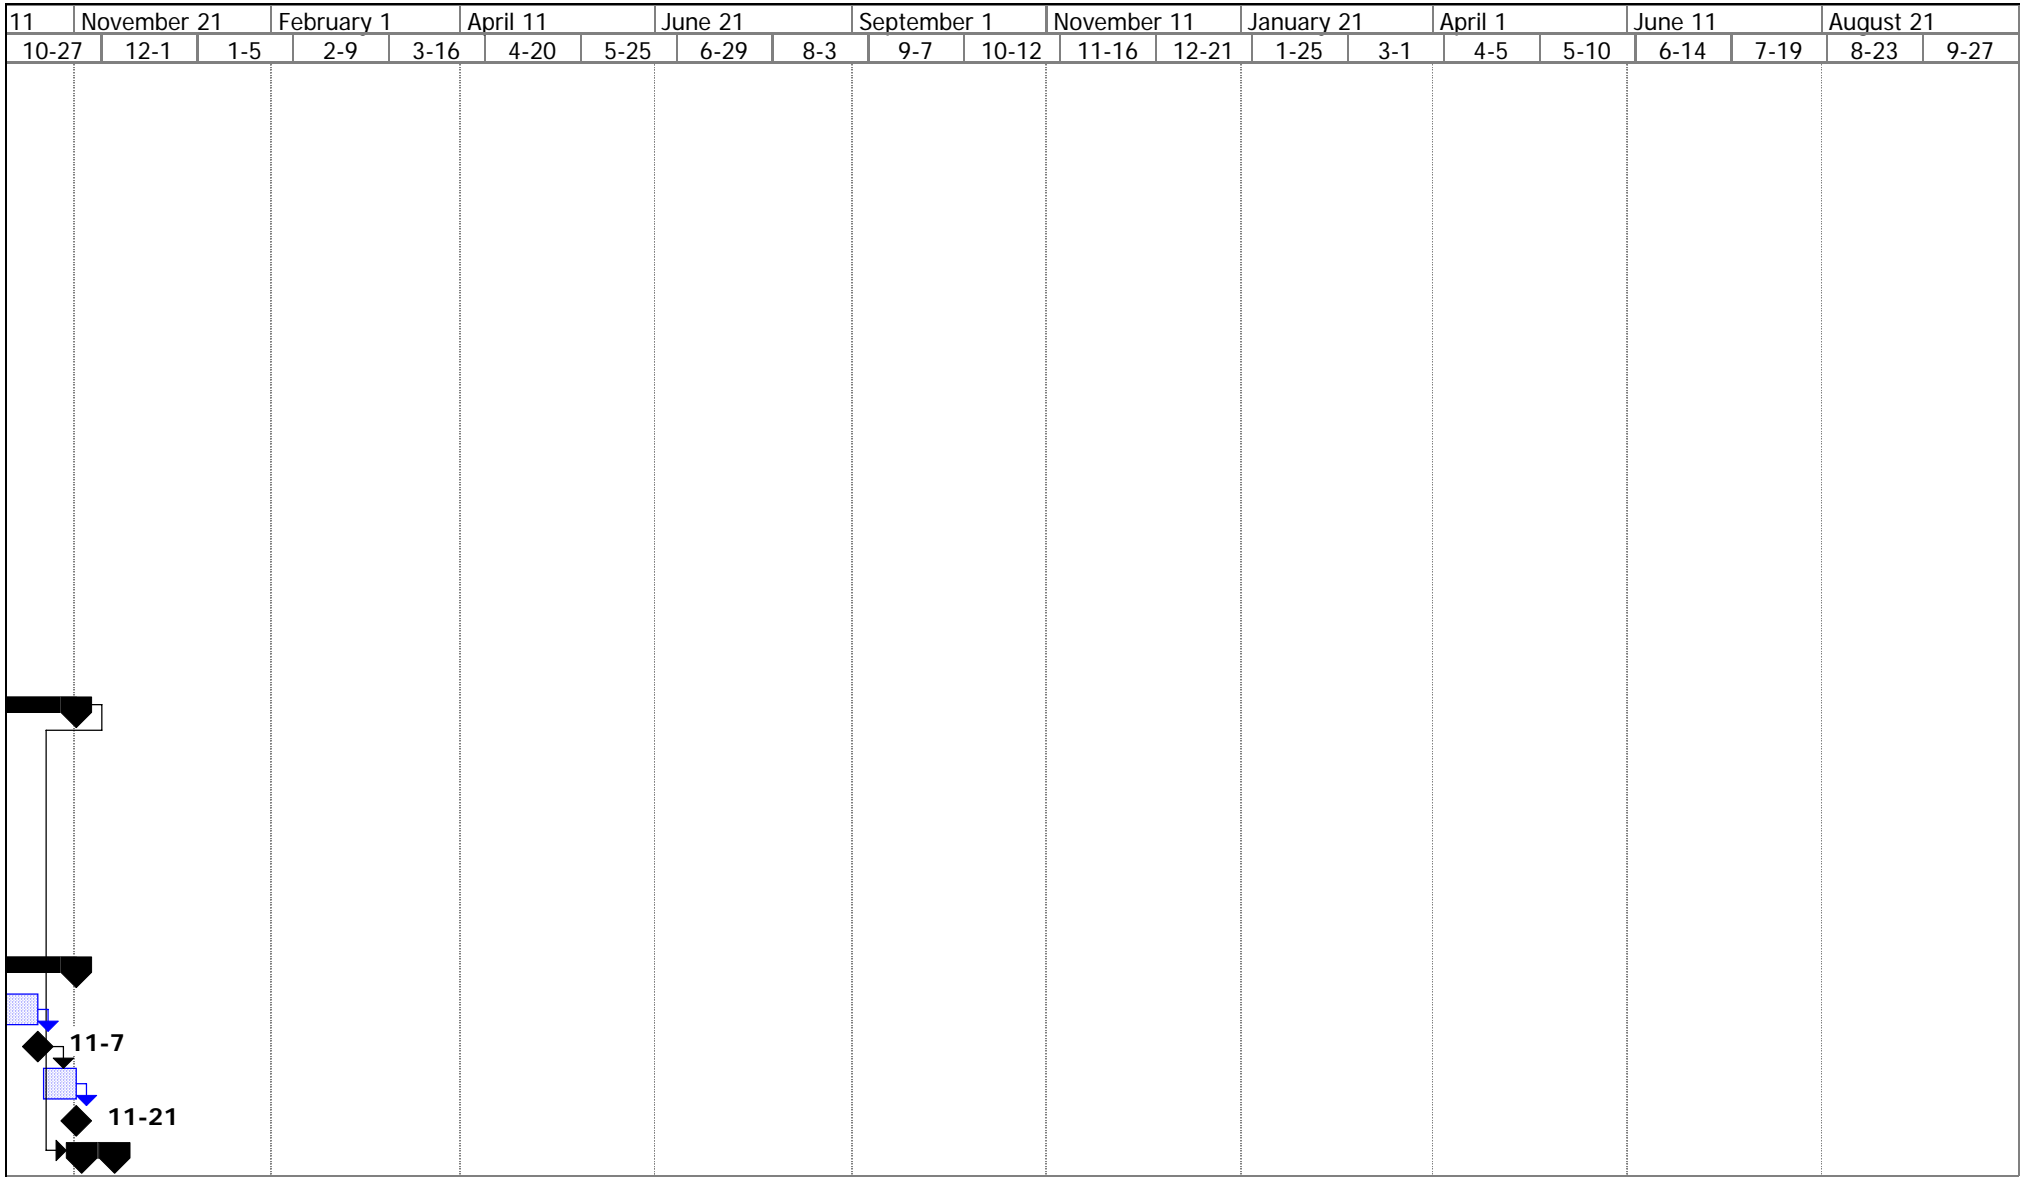

Project: osd20-dev-schedule Date: Tue 08-6-3	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
